



## SARACENS RFC THE REDEVELOPMENT OF THE EXISTING WEST STAND



### MONTHLY NEWSLETTER

Rayner Rowen Construction are pleased to bring you the fourth newsletter on the project and keep you up to date with our progress on the redevelopment of the new West Stand at the StoneX Stadium.

Piling operations are now complete and we have commenced the preparation and pouring of the ground floor raft foundation. The raft foundation will be split into four sections with first concrete pour for the raft foundation will be on 24 June 2021 and then every week thereafter.

The structural steel frame and pre-cast concrete lift shafts will be delivered to site on 05 July and erection will commence for a period of 12 weeks.





## PROGRESS PICTURES





## KEY DATES

The Key Dates have been updated from the last newsletter to include some forthcoming activities.

COMMENCEMENT	15 FEBRUARY 2021
COMPLETION	06 MAY 2022
STRUCTURAL STEELWORK	05 JULY 2021 – 24 SEPTEMBER 2021
METAL DECKING & UPPER FLOORS	03 AUGUST 2021
ROOF CLADDING	27 AUGUST 2021

## SITE ACTIVITIES

Activities over the coming weeks include:

- Raft Foundation / Ground Floor Slab
- Structural Steelwork


## SITE ESTABLISHMENT





## SITE ACCESS

All deliveries and vehicles access and exiting the site will take the following route via Champions Way. This remains unchanged from the previous newsletter.

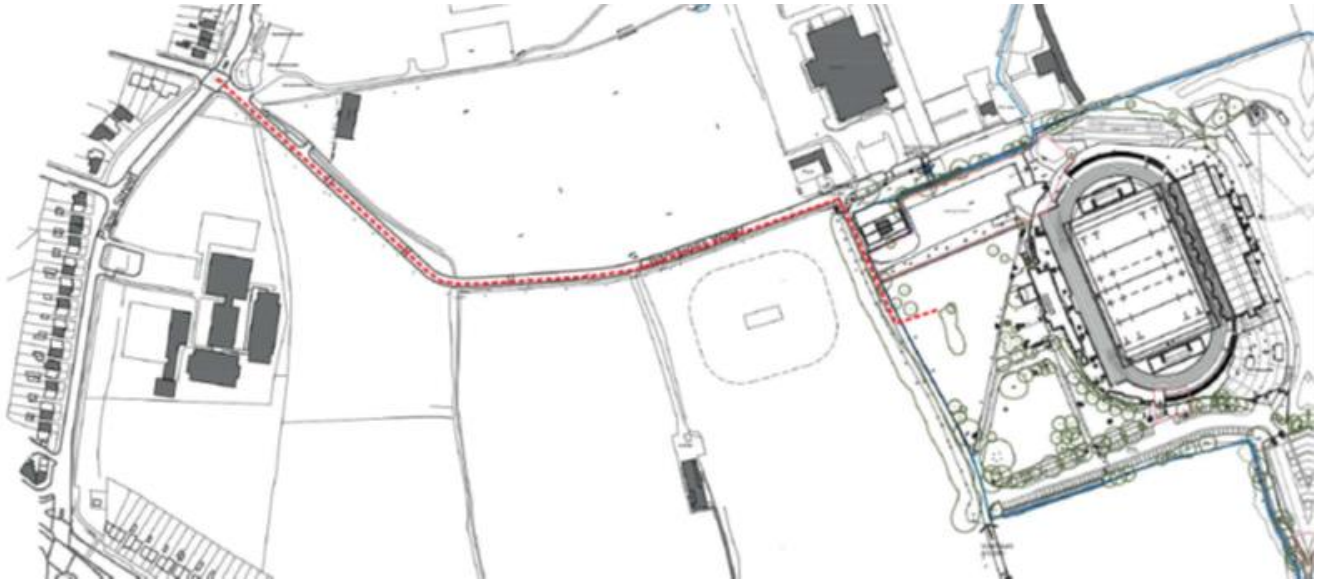

## SITE TEAM

PROJECT DIRECTOR	PROJECT MANAGER	SITE FOREMAN	PROJECT QS
JONATHAN RAYNER	MARTIN PILKINGTON	MICHAEL BURNS	SAM SUTTON

All the project team can be contacted via email at [saracens@raynerrowen.co.uk](mailto:saracens@raynerrowen.co.uk) or on 01257 221 100.

