



SARACENS RFC THE REDEVELOPMENT OF THE EXISTING WEST STAND



MONTHLY NEWSLETTER

Rayner Rowen Construction are pleased to bring you the fifth newsletter on the project and keep you up to date with our progress on the redevelopment of the new West Stand at the StoneX Stadium.


The raft foundation, incorporating the below ground drainage, has been fully poured and the structural steelwork erection has commenced at pace! The steelwork erection now takes place over the next 10 weeks which will also include the installation of the pre-cast concrete lift shafts and stadium terracing. Metal deck packs will also be lifted into place ready for installation in the coming months.

The remaining drainage and ductwork will now commence following completion of the raft along with various external and infrastructure works.





PROGRESS PICTURES

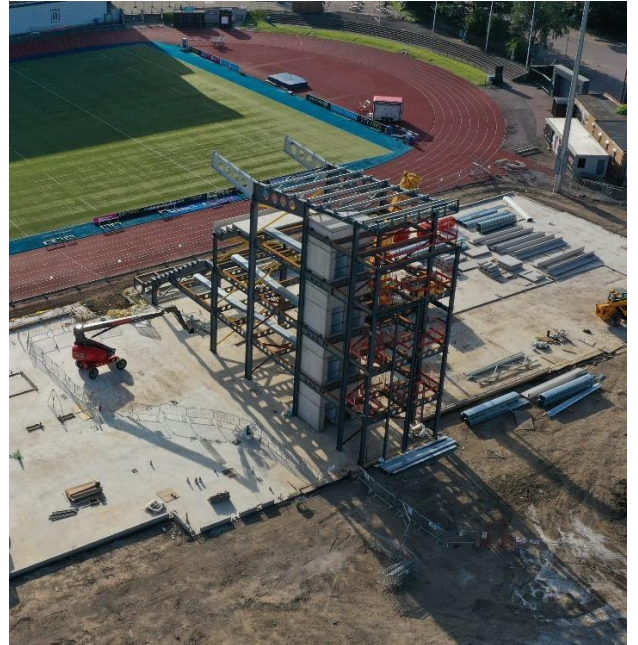



KEY DATES

The Key Dates remain the same from the last newsletter however are included again for clarity.


COMMENCEMENT	15 FEBRUARY 2021
COMPLETION	06 MAY 2022
STRUCTURAL STEELWORK	05 JULY 2021 – 24 SEPTEMBER 2021
METAL DECKING & UPPER FLOORS	03 AUGUST 2021
ROOF CLADDING	27 AUGUST 2021

SITE ACTIVITIES

Activities over the coming weeks include:

- Continuation of the Structural Steelwork erection.
- Installation of the Pre-Cast Concrete Shafts and Terraces.


SITE ESTABLISHMENT

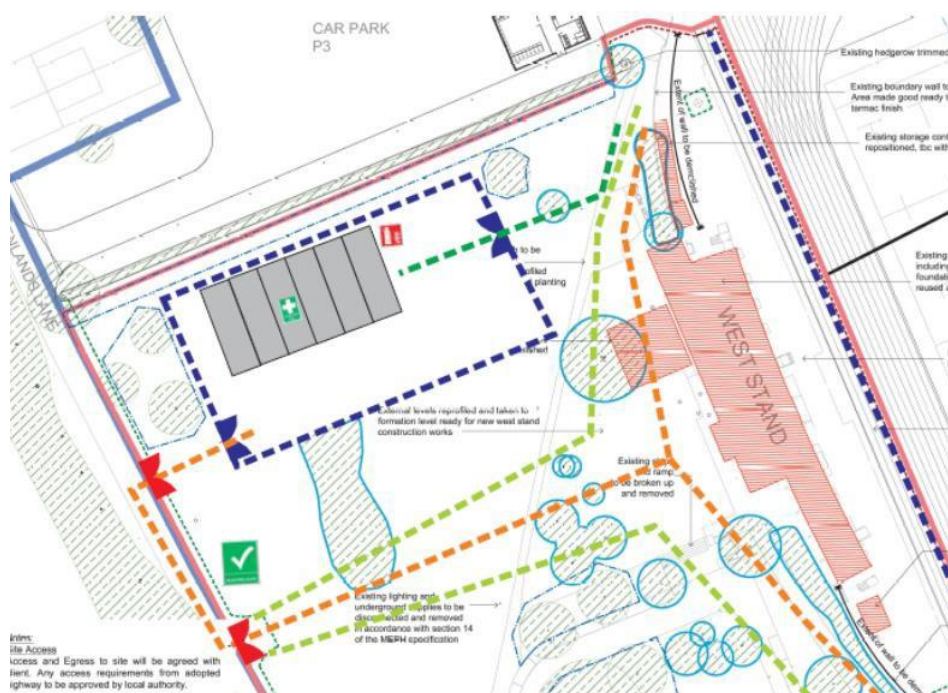



SITE ACCESS

All deliveries and vehicles access and exiting the site will take the following route via Champions Way. This remains unchanged from the previous newsletter.

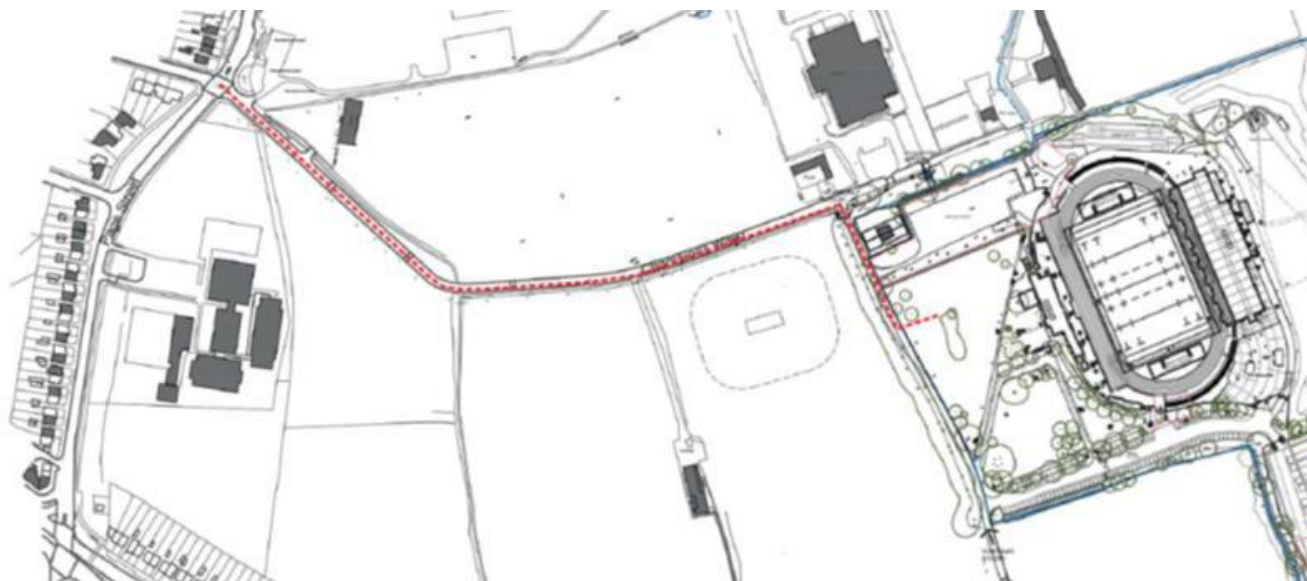

SITE TEAM

PROJECT DIRECTOR	PROJECT MANAGER	SITE FOREMAN	PROJECT QS
JONATHAN RAYNER	MARTIN PILKINGTON	MICHAEL BURNS	SAM SUTTON

All the project team can be contacted via email at saracens@raynerrowen.co.uk or on 01257 221 100.
